Plan: Automate delivery monitoring end to end

P D C A

One Gate Monitoring System | Logistics & Supply Chain | Jun-Oct 2025 | Project lead | SGA 8-step PDCA

THE TARGET

0% → **100%**

Automation today — Target

S **Specific**
Automated, continuous delivery monitoring

M **Measurable**
Automation level from 0% to 100%

A **Achievable**
In-house team skilled in Power BI

R **Reasonable**
OTIF shipment had never reached 90%

T **Time-bound**
5 months, Jun-Oct 2025

ROOT CAUSES (4M ANALYSIS)

1 MACHINE

Monitoring is delayed and not responsive

Manual data processing and no platform for continuous monitoring

2 METHOD

Delivery projection is less accurate

Departure dates (ETD) not updated in the system early

3 METHOD

Non-OTIF is detected too late

No real-time OTIF calculation to flag ETD gaps early

4 METHOD


Stuffing plan is uneven

Schedules not aligned with loading capacity, load never projected

Do: Build One Gate, a live delivery dashboard


P | D | C | A

From manual reports to an automated Power BI platform, completed end of Sep 2025

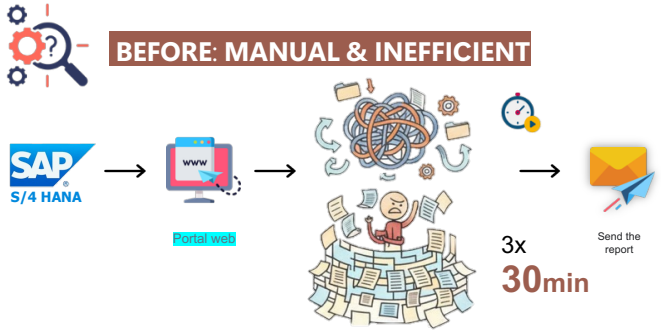

Delayed Monitoring & Response

- Manually **collect** and **clean data** from multiple sources
- Process is **slow** and **time-consuming**
- **High risk of errors** due to manual handling
- Data is **not easily accessible** or portable

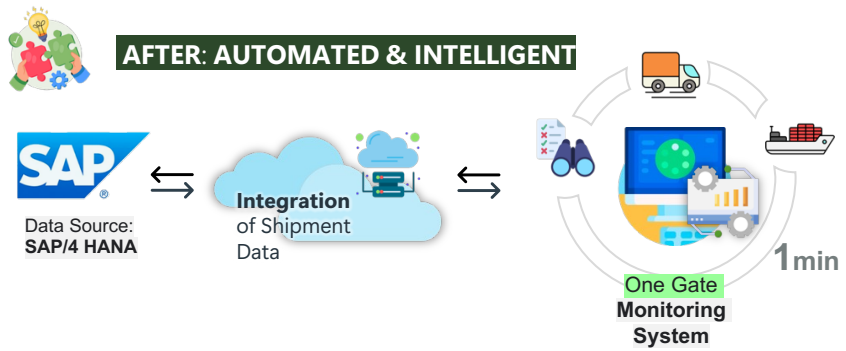

Efficient, Accurate & Responsive

- **Automation** eliminates manual data collection and cleaning
- Supports **faster decision-making** with up-to-date information
- Provides **real-time summary** of outstanding logistics data
- Enables **accessible** & **continuous monitoring** of performance

deliverables



Before vs after, with the dashboard deliverables

1 Continuous monitoring — Cause 1

Automated data feed replaces manual collection and cleaning.

2 ETD matching — Cause 2

Departure dates synced early for accurate projection.

3 Real-time OTIF and GIT — Cause 3

OTIF live; non-OTIF and goods in transit flagged early.

4 Stuffing load projection — Cause 4

Projected trend evens out load against loading capacity.

HOW IT WAS DELIVERED: 5 PHASES, 100% OF PLANNED TASKS COMPLETED

Initiate	Plan	Build and validate	Monitor	Go-live and roll-out
Jun	Jun-Jul	Jul-Sep	Sep-Oct	Oct

Check & Act: Faster monitoring, better delivery

P D C A

Results: October 2025, the first month with the platform live, vs the Jan-Sep 2025 average

C CHECK: RESULTS

Sales volume

+12.6%

vs Jan-Sep average

Export delivery

+12.6%

vs Jan-Sep average

OTIF shipment

88% to 90%

Jan-Sep avg to Oct 2025

Even stuffing

74% to 78%

Jan-Sep avg to Oct 2025

Platform completed end of Sep 2025; one month of data so far.

A ACT: STANDARDIZE, ROLL OUT

Standardized

- Dashboard user guide
- Delivery and shipment arrangement SOP
- Expedite-to-fastest-schedule instruction

Roll-out

Shared with all mill logistics teams and corporate logistics.

Next

Extend scope past DN-out, track vendor allocation, quantify delay impact.

UNLOCKED SKILLS

- Data Analysis
- Logistic & Supply Chain
- Performance reporting
- Power BI
- Problem Solving
- Project Management
